File Name; CIP-UP29

CIP SUMMARY SCHEDULE BY PROJECT - JULY 2011

Data Date:31-Jul-11

Activity ID	Activity Name	Start	Finish	RD
	North Terminal Support	30-Jul-10 A	09-Jan-12	163
Q056A	MIA NORTH TERMINAL ZONE A CONCESSION SPACE	30-Jul-10 A	09-Jan-12	163
Q057A	MIA NORTH TERMINAL ZONE C CONCESSION SPACE	30-Jul-10 A	12-Dec-11	135
	Central Terminal	27-Aug-07 A	20-Feb-14	936
A155B1	MIA FRONT TERMINAL D-H FIRE SPRINKLER AND FIRE ALARM ...	27-Apr-11 A	24-Oct-11	86
A155B2	MIA BACK TERMINAL D-H LIFE SAFETY UPGRADES AREA 1	20-Mar-11 A	20-Feb-14	936
A155B3	MIA BACK TERMINAL D-H LIFE SAFETY UPGRADES AREA 2	20-Mar-11 A	20-Feb-14	936
A155B4	MIA BACK TERMINAL D-H LIFE SAFETY UPGRADES AREA 3	20-Mar-11 A	20-Feb-14	936
K086A	MIA CENTRAL TERMINAL TENANT RELOCATIONS	29-Aug-07 A	29-Aug-11	30
M115A	MIA RELOCATION OF AIRLINES/TENANTS INTO CENTRAL TERMI..	27-Aug-07 A	29-Aug-11	30
M113A	MIA Cc F RESTROOM EXPANSION 7 CONCESSION SHELL WORK	12-Jun-11 A	29-Nov-11	122
	Concourse E	30-Nov-10 A	11-Nov-11	104
F117A	MIA CC E FIRE SPRINKLER AND FIRE ALARM UPGRADES	30-Nov-10 A	11-Nov-11	104
	South Terminal Support Projects	01-Jan-93 A	30-Sep-12	305
K151A	MIA Cc J A380 MODIFICATIONS	01-Sep-10 A	24-Oct-11	60
L118B	MIA Cc J CLUB AMERICA	30-Mar-11 A	04-Oct-11	66
M018A	MIA SOUTH TERMINAL SUPPORT PROJECT (NON-POJV WORK)	01-Jan-93 A	30-Sep-12	428
	Other Terminal Projects	01-Jan-04 A	16-Nov-11	109
B327A	CONCESSIONS	01-Jan-04 A	30-Sep-11	62
B392B	MIA TERMINAL SEATING & MISCELLANEOUS FURNITURE	20-May-04 A	16-Nov-11	109
C154A	MIA PASSENGER LOADING BRIDGE PROCUREMENT	14-Apr-11 A	28-Oct-11	90
	Airside	01-Apr-06 A	30-Oct-11	92
H024C-1	MIA RUNWAY 8R/26L PAVEMENT RECONSTRUCTION	20-May-11 A	09-Aug-11	10
J005A	MIA FAA FIBER OPTIC LOOP	01-Apr-06 A	30-Oct-11	92
	Landside	23-May-07 A	14-Sep-13	555
B051A	MIA IMPROVEMENTS 67TH & PERIMETER RD. NORTH	07-Jun-11 A	07-Mar-12	221
D105B	MIA FLAMINGO & DOLPHIN GARAGES PAINTING	15-May-11 A	13-Aug-11	14
H063A	MIA TERMINAL LVD & UVD ACCESSIBILITY IMPROVEMENTS	08-Jul-11 A	06-Jun-12	312
J012A	MIA FIRE UPGRADES SECURITY / COMM. RMS (10)	22-Jul-10 A	05-Dec-12	494
K001C	COMMISSARY WAREHOUSE BUILDING DEMOLITION	30-Jul-10 A	29-Sep-11	61
K001G	SWAP OF PARCELS A & B TO ENABLE THE BUS MAINTENANCE ...	31-Jul-07 A	27-Mar-12	172
K069B	MIA HOTEL 8TH FLOOR POOL DEMOLITION	18-Jul-11 A	08-Jan-12	162
M043A	OPF INTERSECTION LEJUNE & CURTIS ROAD IMPROVEMENTS	19-Feb-11 A	08-Oct-11	70
N022A	MIA QUICK RESPONSE RENOVATIONS	23-May-07 A	17-Sep-11	49
N144A	MIA BUILDING 704 MISCELLANEOUS REPAIRS	16-May-11 A	04-Nov-11	97
N145A	MIA BUILDING 845 MISCELLANEOUS REPAIRS	02-Apr-11 A	28-Sep-11	60
N146A	BUILDING 3040 MISCELLANEOUS REPAIRS & PARKING LOT IMP...	25-Jul-11 A	08-Aug-11	9
N147A	BUILDING 3050 MISCELLANEOUS REPAIRS	20-May-11 A	25-Nov-11	118
N165B	MIA BUILDING 896 PAINT BOOTH	29-Nov-10 A	29-Nov-11	122
N165C	MIA BUILDING 896 40 YR RECERTIFICATION	14-Dec-10 A	14-Sep-13	777
O141A	MIA PARKING FACILITY REVENUE COLLECTION SYSTEM UPGR...	18-Jan-11 A	28-Oct-11	90
P134A	MIA WESTSIDE FUMIGATION PROJECT	17-Apr-11 A	01-Feb-12	186
P159A	MIA PARK & RIDE IMPROVEMENTS	22-Jul-11 A	03-Apr-12	177
	MIA Mover	10-Mar-09 A	05-Mar-12	149
J104A	MIA MOVER PROGRAM - DBOM	10-Mar-09 A	05-Mar-12	149
	Environmental	01-Jul-94 A	30-Sep-15	1523
91068M93	MIA & GA Enviromental Regulatory Compliance Service	01-Jul-94 A	30-Sep-15	1523
B385A	MIA & GA MISCELLANEOUS ASBESTOS REMOVAL	15-May-02 A	18-Jun-12	324
H032A	MIA WEST SIDE BOOSTER PUMP STATION	11-Apr-11 A	21-Jan-12	175
N119A	MIA WATER DISTRIBUTION SYSTEM INFRASTRUCTURE IMPROV...	10-Mar-09 A	29-Apr-15	1369
CIP194.18	ADF ENVIRONMENTAL POLLUTION	30-Sep-95 A	30-Sep-15	1523
CIP571	MIA & GA ENVIRONMENTAL PROGRAM	01-Sep-08 A	30-Sep-15	1523
Q071A	SUPPORT SERVICES FOR CENTRAL BLVD. CONSTRUCTION	29-Apr-10 A	29-Oct-12	457
Q017A	MIA STORMWATER MASTER PLAN	20-Aug-10 A	20-Aug-13	752
Q016A	MIA SANITARY SEWER MASTER PLAN	30-Jun-09 A	29-May-12	304
Q015A	MIA WATER MASTER PLAN	03-Nov-09 A	09-Nov-12	468
	Security	26-Jan-09 A	16-Dec-13	621
G004A	MIA Cc E - G, J, & ST CHECKPOINTS SECURITY SCREENS	22-May-10 A	21-Feb-13	572
I111C-1	OPF SECURITY ENHANCEMENT PROJECT	11-Oct-10 A	12-Sep-11	44
I145A	MIA TERMINAL ADDITIONAL ACCESS CONTROL DEVICES PKG 2	12-Apr-11 A	16-Dec-13	621
I161A	FUEL STORAGE FACILITY, INTRUSION DETECTION	26-Jan-09 A	23-Feb-13	574
	Business Systems	30-Jun-08 A	29-Aug-12	396
I113A	MIA CUTE (COMMON USE TERMINAL EQUIPMENT)	30-Jun-08 A	29-Aug-11	30
I114A	MIA BUILDING MANAGEMENT SYSTEMS	02-Feb-09 A	18-Dec-11	141
I143A	MIA PREMISE DISTRIBUTION SYSTEM	17-Mar-09 A	29-Aug-12	396
L057A	MIA TERMINAL WIDE WIRELESS DATA DEPLOYMENT	25-Aug-09 A	10-Feb-12	195
	Support Projects / Contingency	01-Jan-05 A	31-Mar-12	245
I194A	MIA WASTE COMPACTOR	14-Jan-06 A	11-Oct-11	73
K098A	MIA WAYFINDING SIGNAGE PROGRAM	01-Jan-05 A	11-Nov-11	104
M118A	MCC-7-2005	04-May-10 A	31-Mar-12	245
N115A	COST ESTIMATING & SCHEDULING SERVICES CONSULTANTS	05-Dec-07 A	05-Dec-11	128
	Northside Redevelopment	31-Dec-09 A	28-Sep-11	60
B027A	MIA USDA/APHIS FACILITY	31-Dec-09 A	05-Sep-11	37
F178A	MIA TRACT ONE DRAINAGE, GRADING & PAVEMENT IMPROVEM...	30-Apr-11 A	28-Sep-11	60
L016A	MIA UPS MIAMI AIRPORT BUILDING	21-May-11 A	18-Sep-11	50
	General Aviation Airports	01-Jan-93 A	30-Sep-15	1523
95002O93	General Aviation Airport Environmental Compliance	01-Jan-93 A	30-Sep-15	1523
95096O93	ENVIRONMENTAL POLLUTION ABATEMENT	06-Jan-97 A	30-Sep-15	1523
L085A	OPF CONSTRUCT NEW AIR TRAFFIC CONTROL TOWER	15-Apr-10 A	26-Jan-12	180
L141A	TMB RUWAY 9R/27L EXTENSION	01-Jun-10 A	03-Feb-12	188

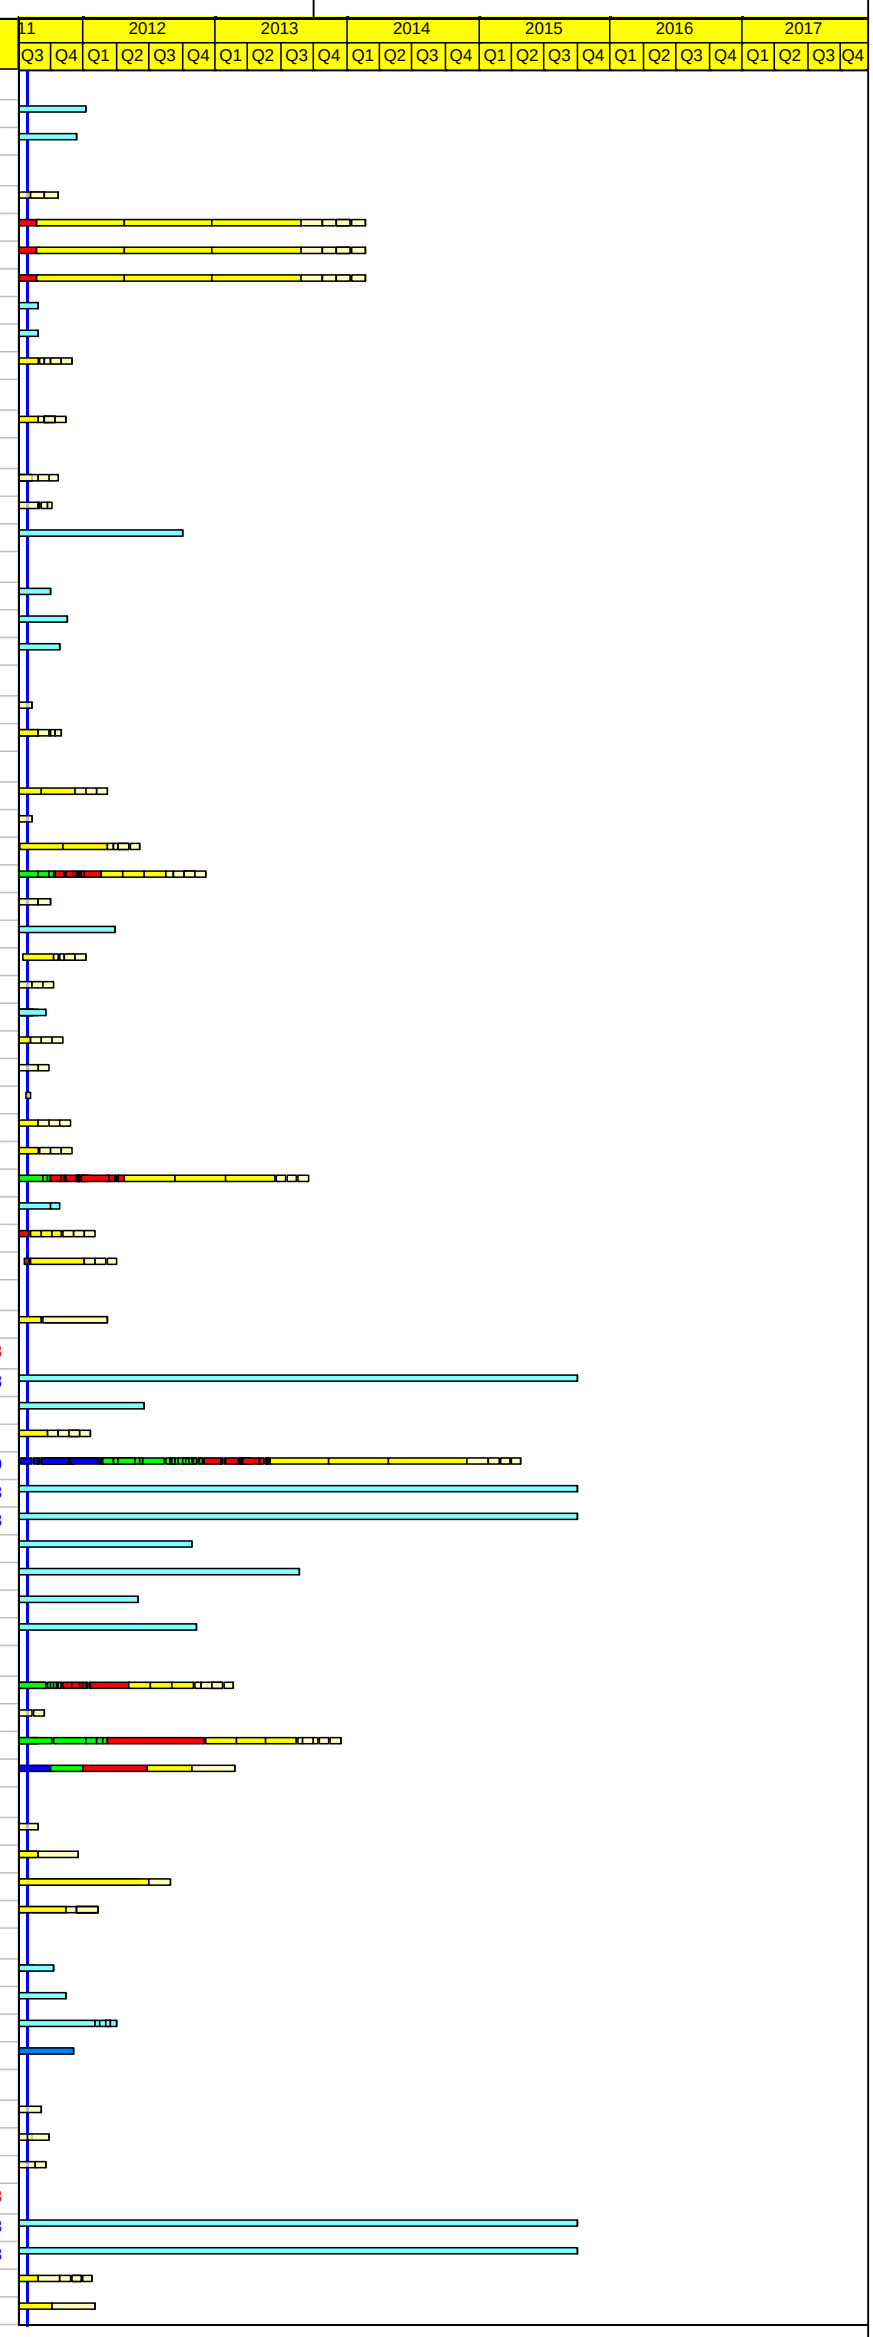

Planning | Bid & Award | Closeout | Budget Reserves
Design | Construction | Cash Flow | Milestone

Layout : 003 - CIP SUMMARY BY PROJECT

© Primavera Systems, Inc.
